



# **San Ysidro Land Port of Entry Modernization**

## **Community Representative Committee Meeting**

***U.S. General Services Administration***


*December 10<sup>th</sup>, 2013*

*San Diego, California*

# San Ysidro LPOE Phasing Plan

## FINAL CONCEPT

-  NEW BUILDINGS & STRUCTURES  
 NEW CANOPY

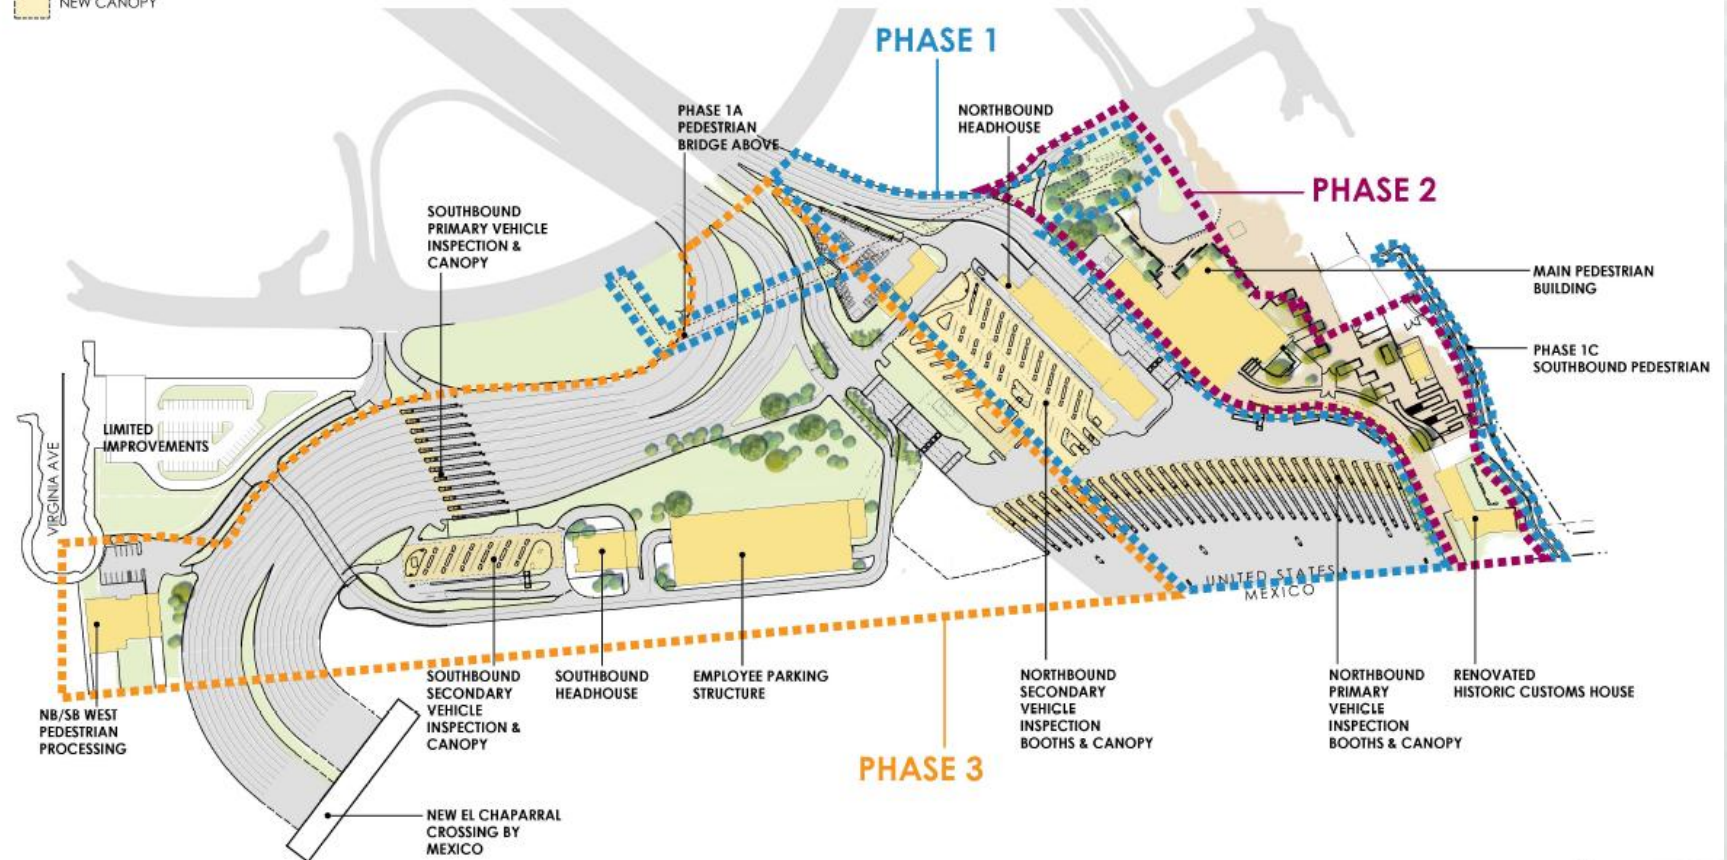



# San Ysidro LPOE Master Plan



# Timeline

- **PHASE 1**

- Head House completion Spring 2014
- Primary Canopy completion Summer 2014
- Phase 1B project completion Fall 2014
- Phase ID Ped West Facility Fall 2015

- **PHASE 3**

- 30 months of construction duration  
(Currently unfunded, but included in the President's FY 2014 Budget)

- **PHASE 2**

- 36 months of construction duration  
(Currently unfunded)

# Phase 1

## Progress Photos



# San Ysidro – November 2013






# Completed – North Secondary



# Completed – East Pedestrian Crossing

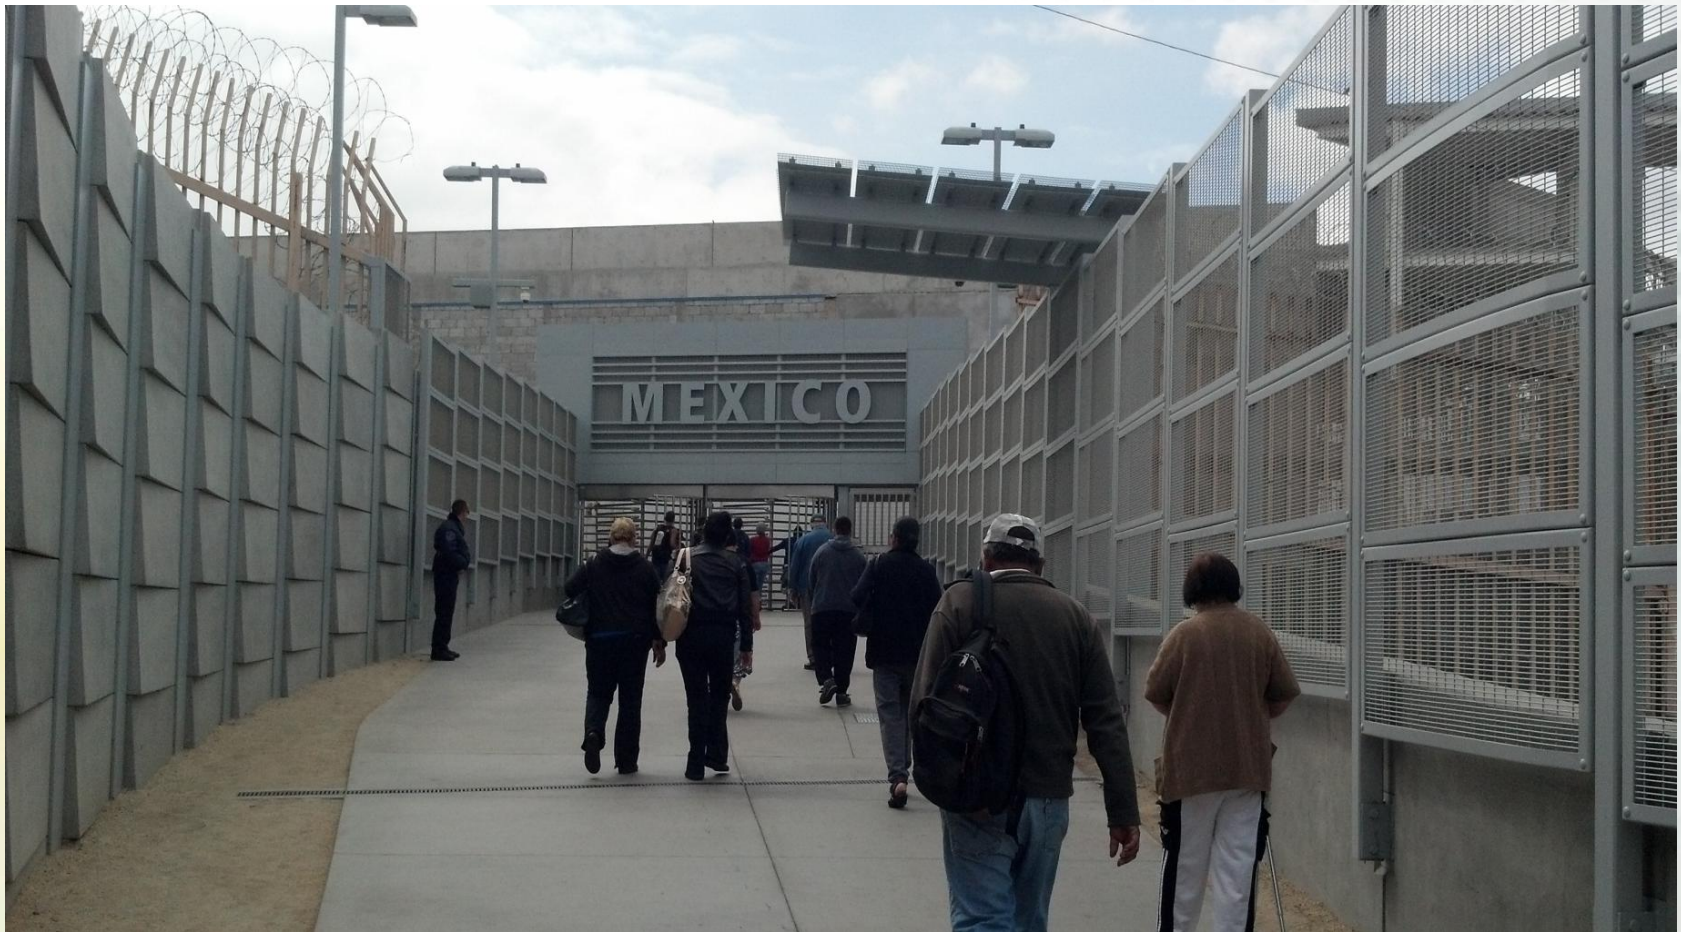



# Completed – Temporary Connection to El Chaparral



# Phase 1

## Construction (*Active*)



# Primary Canopy Erection in Progress



# Primary Canopy Erection in Progress





# Headhouse Construction in Progress



## San Ysidro - Results





## San Ysidro – What's Next




# PedWest Facility & Proposed Transit Facility




## Regional Concept (“Concept One”)

Proposed Transit Center with necessary modifications

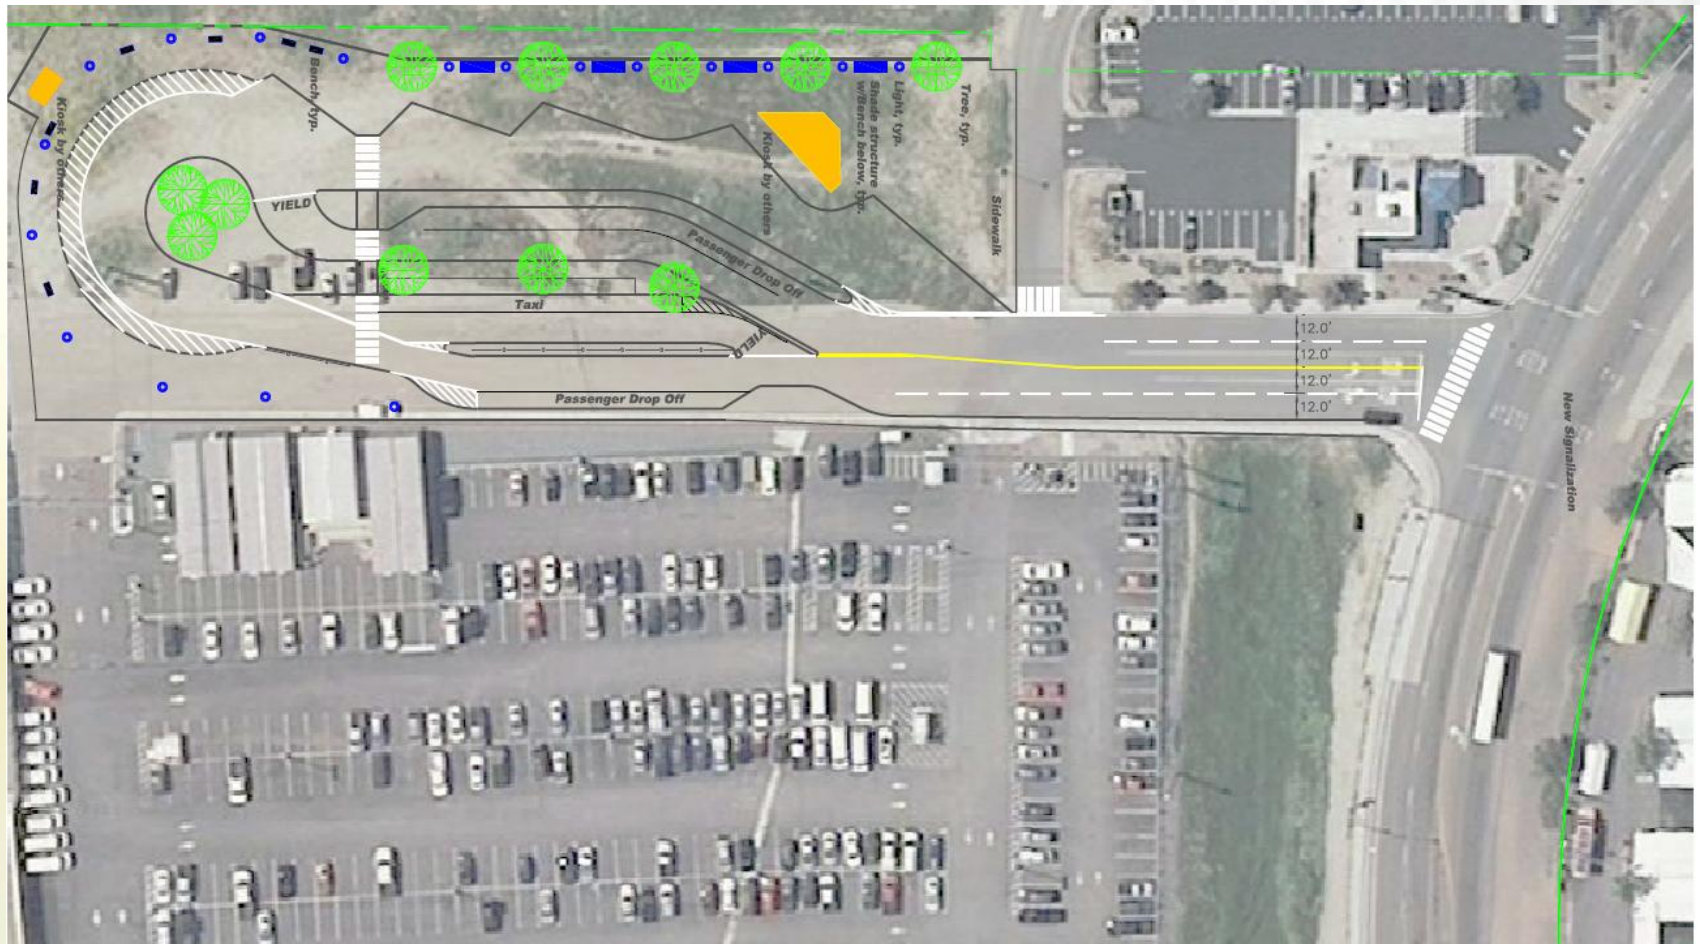

# PedWest – New Virginia Avenue Pedestrian Facility

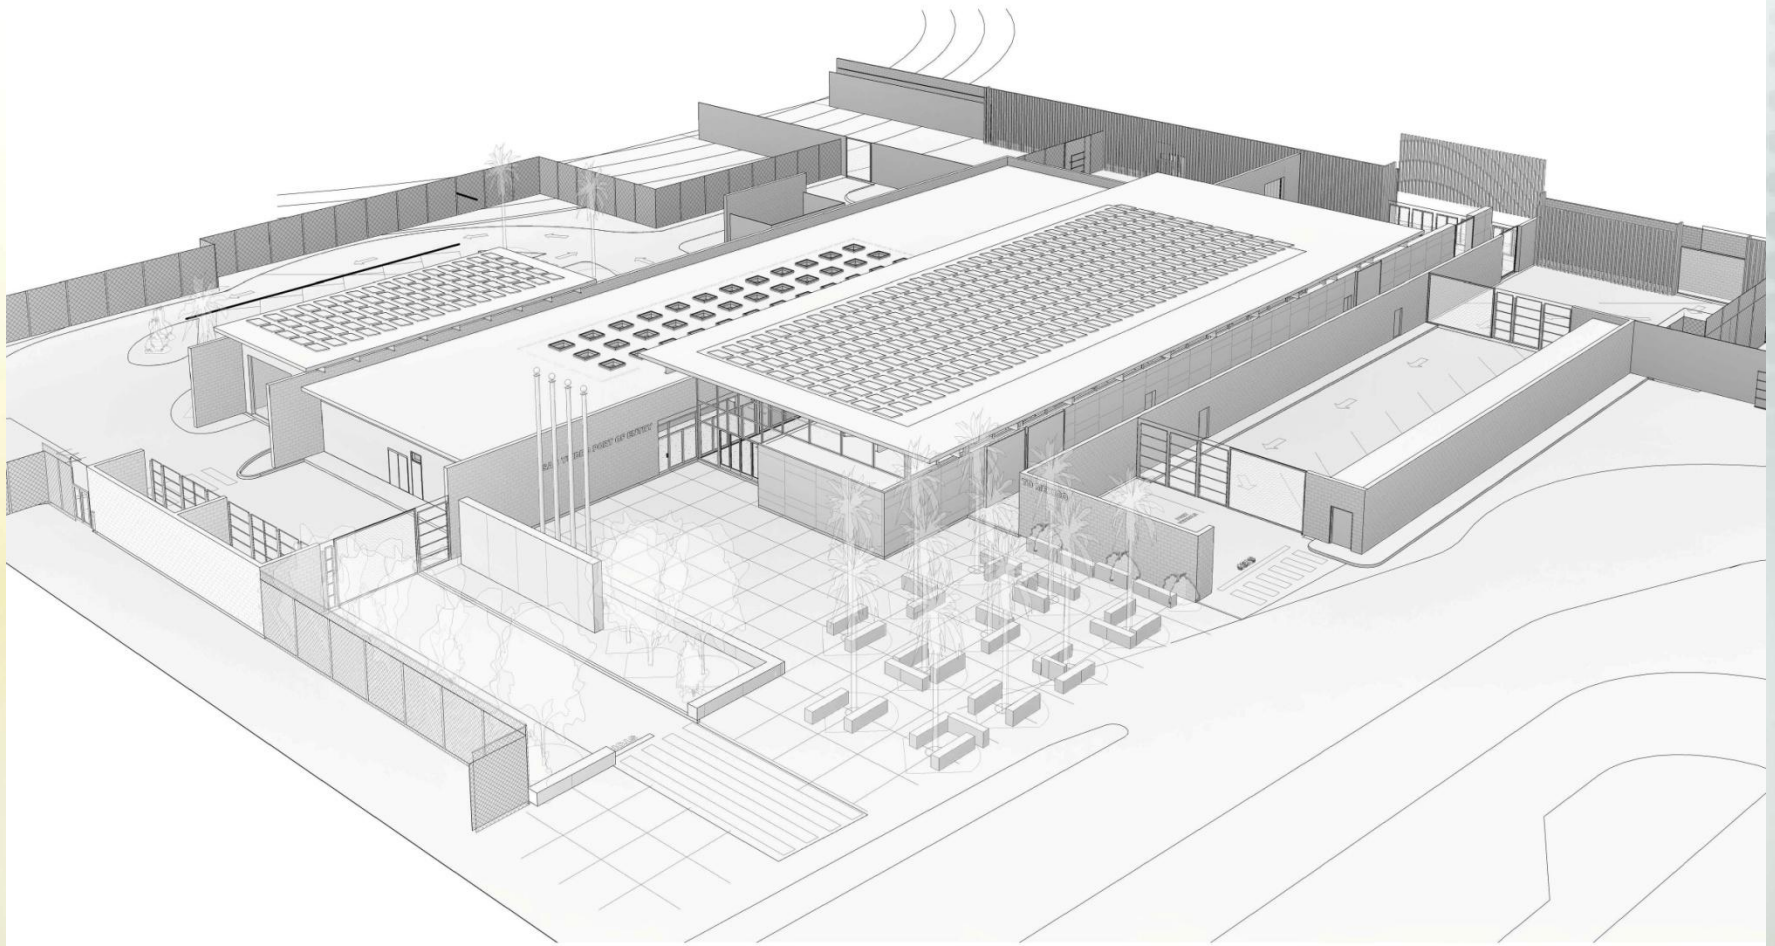



# New Pedestrian Crossing & Proposed Transit Center

What's been accomplished:

- NEPA Process underway
- Stakeholder Kick Off
- Regional Agreement on Preliminary Concept
- Funding Concept Identified
- General Agreement on Design Process
- Initial draft of Regional MOU distributed to partners

# New Pedestrian Crossing & Proposed Transit Center

## Schedule:

- Regional Kick Off 4/13
- EIS Scoping Meeting 5/9/13
- MOU Execution Est. 12/2013
- DSEIS Public Hearing 11/14/2013
- Design and Construction Procurement 2/2014
- Virginia Avenue Public Workshop 4/2014
- Completion Fall 2015



**QUESTIONS?**
