




U.S. Land Port of Entry Expansion and Modernization

Project Management Division
Alexandria Bay, New York | March 2022



New progress

- Main Building, Secondary Inspection Building, Inspection Booth, and Phase Two Parking Deck punch list work is nearing completion.
- Tenant IT equipment installation is underway and nearing completion.
- Received site lighting custom brackets and installation coordination is underway.
- Completed furniture installation. Minor adjustments are underway.
- Complete site cleanup and equipment removal in time for the relocation and Go Live.
- Planned relocation from the existing Administration Building for March 14 and 15.
- Go Live is planned for March 17.



A view looking southeast at the Phase Two buildings and non-commercial inspection lanes. (Photo courtesy of Revette Studio)

Look ahead


- Scheduled relocation of staff from the existing Administration Building to the new Main Building for March 14 and 15.
- Begin passenger vehicle traffic processing through the new lanes on March 17.
- Begin CBP Decommissioning of the existing Administration Building as soon as relocation and Go-Live are complete.

Project facts

- **Scope:** Facility-wide modernization and expansion.
- **Cost:** \$215 million
- **Congressional appropriations:** Phase one funding appropriated in [fiscal year 2016 budget](#).
- Phase two funding appropriated in fiscal year 2018 in the amount of approximately \$133 million.
- **Contract:** Awarded in June 2017 to Northland/Cianbro Joint Venture.

Advisories

- Strict policies have been put into place to prevent exposure to COVID-19 at the construction site.
- There will be no access to the site without first checking in with Northland | Cianbro and following their safety procedures.
- Please report any exposures to a member of the project staff promptly so that appropriate measures can be taken.

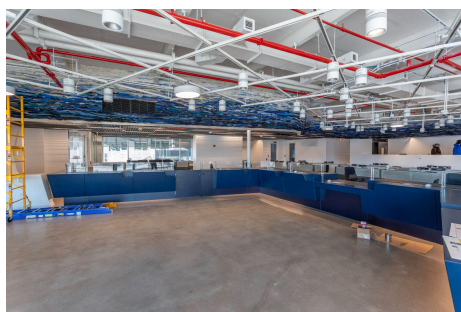

A view of the new passenger inspection lobby. (Photo courtesy of Revette Studio)

Project estimated timeline

- **March 14-15 2022** - Relocation of staff from the existing Administration Building to new Main Building.
- **March 17 2022** - Main Building and Passenger Inspection Lanes Go-Live.
- **August 2022** - Substantial completion of Phase Two.
- **September 2022** - Contract completion.

For more information

Andrew Woodring, GSA Project Manager
Andrew.Woodring@gsa.gov
315-448-0928
gsa.gov/alexbaylpoe
