




U.S. Land Port of Entry Expansion and Modernization

Project Management Division
Alexandria Bay, New York | May 2020



New progress

- Installed secondary inspection canopy structural steel and roof decking.
- Demolished the existing secondary inspection canopy.
- CBP has started testing operations in the new Non-Intrusive Inspection Building.
- New York State Department of Environmental Conservation has provided the underground storage tank registration allowing the emergency generator to operate fully.
- Begun work on the retaining wall between I-81 northbound and southbound.
- Construction of the foundations, structural steel, and roof decking of the Main Building is ongoing.
- Installed roof joists and decking at the new APHIS building.
- Installed LED signs at the Phase One inspection lanes.



An aerial view looking north at construction of the secondary inspection canopy and new Main Building. (Photo courtesy of Revette Studio)

Look ahead


- Substantial completion of the Non-Intrusive Inspection Building will occur by the end of the month.
- Stairs are being installed at the Main Building and Outbound Building.
- Started paving on County Road 191.
- All southbound traffic has been routed through the existing commercial lanes to allow construction of the final parking deck columns.

Project facts

- **Scope:** Facility-wide modernization and expansion.
- **Cost:** \$215 million
- **Congressional appropriations:** Phase one funding appropriated in [fiscal year 2016 budget](#).
- Phase two funding appropriated in fiscal year 2018 in the amount of approximately \$133 million.
- **Contract:** Awarded in June 2017 to Northland/Cianbro Joint Venture.

Advisories

- Strict policies have been put into place to prevent exposure to COVID-19 at the construction site.
- There will be no access to the site without first checking in with Northland | Cianbro and following their safety procedures.
- Please report any exposures to a member of the project staff promptly so that appropriate measures can be taken.

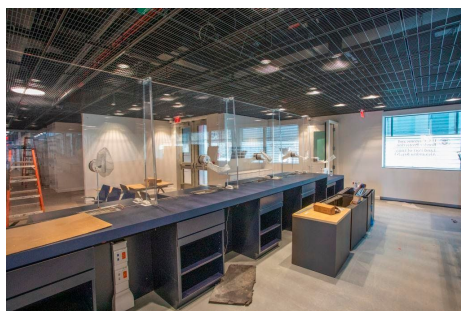

A view of the new commercial building transaction counter installation (Photo courtesy of Revette Studio)

Project estimated timeline

- **June 15, 2020** - Substantial completion for the Commercial Building.
- **August 2020** - APHIS Building substantial completion.
- **August 2022** - Substantial completion of Phase Two.
- **September 2022** - Contract completion.

For more information

Andrew Woodring, GSA Project Manager
Andrew.Woodring@gsa.gov
315-448-0928
gsa.gov/alexbaylpoe
