



GSA Transition Coordination Center

EIS Transition

Progress Tracking Report Dashboard for the period ending January 31, 2021

Version 1.0

February 25, 2021

DTID: #TCC2-ASC-0072-20210225-00

PREPARED FOR
**Transition Coordination Center
General Services Administration
Federal Acquisition Service
1800 F Street NW
Washington, DC 20405**

**Contract Number: GS00Q12NSD0002
Order Number: 47QTCB20F0073**

Document Change History

Version	Description	Date	Prepared By
1.0	Original Submission	02/25/2021	Ken Palmer

Table of Contents

1	INTRODUCTION	3
2	TRANSITION STATUS	3
2.1	TRANSITION VOLUME	3
2.2	TRANSITION PROGRESS METRICS SUMMARY	5
2.3	AGENCY TRANSITION SCORECARDS	5
2.4	TRANSITION COMPLETION STATUS	8
3	FAIR OPPORTUNITY SOLICITATIONS	8
3.1	FAIR OPPORTUNITY PROCESS FOR SELECTING EIS CONTRACTORS	8
3.1.1	<i>Fair Opportunity Solicitations Passed GSA In-Scope Review</i>	9
3.1.2	<i>Fair Opportunity Solicitations Issued to Industry</i>	11
3.1.3	<i>EIS Task Orders Awarded</i>	13
4	TRANSITION EXECUTION PROGRESS	13
4.1	GOVERNMENT-WIDE	14
4.2	TRANSITION PROGRESS – AGENCY CATEGORY	14
4.2.1	<i>Transition Progress - Large Agencies</i>	15
4.2.2	<i>Transition Progress - Medium Agencies</i>	16
4.3	TRANSITION CLOSEOUT	16
	APPENDIX A – ACRONYMS	18
	APPENDIX B – TRANSITION COMPLETION STATUS: SMALL AGENCIES INCLUDING NATIVE AMERICAN TRIBES	20
	APPENDIX C – TRANSITION PROGRESS MILESTONES GANTT CHART	22
	APPENDIX D – KEY METRICS	23
	APPENDIX E – KEY DEFINITIONS	24

List of Tables

TABLE 1.	<i>TRANSITION PROGRESS METRICS SUMMARY: AGENCY CATEGORIES</i>	5
TABLE 2.	<i>EIS TRANSITION SCORECARD: LARGE AGENCIES</i>	6
TABLE 3.	<i>EIS TRANSITION SCORECARD: MEDIUM AGENCIES</i>	7
TABLE 4.	<i>TRANSITION COMPLETION STATUS: LARGE AND MEDIUM AGENCIES</i>	8
TABLE 5.	<i>FAIR OPPORTUNITY SOLICITATION PROGRESS</i>	8
TABLE 6.	<i>EIS TASK ORDER AWARD STATUS: LARGE AGENCIES</i>	13
TABLE 7.	<i>EIS TASK ORDER AWARD STATUS: MEDIUM AGENCIES</i>	13

List of Figures

FIGURE 1.	<i>SIR # ACTIVE: GOVERNMENT-WIDE</i>	4
FIGURE 2.	<i>FO SOLICITATIONS # EXPECTED AND FO SOLICITATIONS # PASSED GSA IN-SCOPE REVIEW: LARGE AGENCIES</i>	9
FIGURE 3.	<i>FO SOLICITATIONS # EXPECTED AND FO SOLICITATIONS # PASSED GSA IN-SCOPE REVIEW: MEDIUM AGENCIES</i>	10
FIGURE 4.	<i>FO SOLICITATIONS # EXPECTED AND FO SOLICITATIONS # ISSUED TO INDUSTRY: LARGE AGENCIES</i>	11
FIGURE 5.	<i>FO SOLICITATIONS # EXPECTED AND FO SOLICITATIONS # ISSUED TO INDUSTRY: MEDIUM AGENCIES</i>	12
FIGURE 6.	<i>QUARTERLY TRENDING % COMPLETE: GOVERNMENT-WIDE</i>	14
FIGURE 7.	<i>SIR # ACTIVE – BASELINE TO CURRENT: LARGE AGENCIES</i>	15
FIGURE 8.	<i>SIR PWV # ACTIVE – BASELINE TO CURRENT: LARGE AGENCIES</i>	15
FIGURE 9.	<i>SIR # ACTIVE – BASELINE TO CURRENT: MEDIUM AGENCIES</i>	16
FIGURE 10.	<i>SIR PWV # ACTIVE – BASELINE TO CURRENT: MEDIUM AGENCIES</i>	16
FIGURE 11.	<i>LIMITING USERS STATUS</i>	17
FIGURE 12.	<i>LIMITING USERS CUMULATIVE PROGRESS</i>	17

1 Introduction

1.1 Purpose

The General Services Administration (GSA) Transition Coordination Center (TCC) created the Enterprise Infrastructure Solutions (EIS) Transition Progress Tracking Report (TPTR) Dashboard to provide a high-level monthly overview of transition progress from the expiring Networx, Washington Interagency Telecommunications System (WITS) 3, and GSA Regional local service (RLS) contracts to EIS or other contract vehicles. The charts contained herein were specifically selected by a collaboration team made up of agency, EIS contractor, and GSA representatives and briefed to the Infrastructure Advisory Group (IAG), to communicate transition progress at the Government-wide and agency levels, while highlighting large and medium agencies.

This month's report is derived from acquisition planning and decision data, Transition Inventory (TI) data, and other supporting data as of January 31, 2021. Business Volume (BV) reflects data as of December 31, 2020.

Note: *GSA extended Networx, WITS 3, and GSA RLS contracts to remove potential timeline barriers for modernization and transition execution with commitment by agencies to maintain momentum on EIS transition and network modernization. EIS transition milestones and target dates have been updated herein.*

1.2 Agency Categories and Size Standards

There are currently over 200 agencies with TI and billing under the expiring contracts. For this report, agencies are categorized into three groups: large agencies, medium agencies, and small agencies as defined by their average annual BV on the Networx contracts in FY12 through FY15.

- Large agencies: 17 agencies with annual BV \geq \$10 million
- Medium agencies: 25 agencies with annual BV $<$ \$10 million but \geq \$1 million
- Small agencies: 179 agencies with annual BV $<$ \$1 million (117 agencies including AB Code 0022 which represents the 62 Tribal Nations as a single entity and AB Code 0047 which includes all GSA-Regional Internal data in this report).

2 Transition Status

Transition volume, counts, scorecards, and completion status provide a snapshot of progress against transition tracking metrics. Given the agency inventory confirmation deadline was October 31, 2016, baseline data as of November 1, 2016 has been used to develop trend analysis. Additional information pertaining to Transition Completion Status of Small Agencies including Native American Tribes may be found in Appendix B; Transition Progress Milestones are shown in Appendix C; Key Metrics are described in Appendix D; and other Key Definitions are available in Appendix E.

2.1 Transition Volume

Transition volume provides a count of active Service Instance Records (SIRs) in TI beginning on November 1, 2016 through the current period. When SIRs are weighted based on their complexity to transition, it is referred to as SIR Proportional Weighted Value (PWV). Since the

volume of active SIRs and current BV are indicators of agency transition completion status (Section 2.3), GSA's TCC will report on the volume of services remaining on expiring contracts and the associated BV until both volumes are zero.

Figure 1 illustrates trending active SIR counts and target active SIR counts required to drive the active inventory on expiring contracts to zero by the milestone dates. The difference between actual active and target active SIR counts indicates the number of SIR disconnects. To meet the transition milestones, agencies must have SIR PWV 50% disconnected by March 31, 2021, 90% by March 31, 2022, and 100% disconnected by September 30, 2022.

This Key identifies the markings used when viewing SIR # Active: Government-wide.

Key	
■	SIRs # Active (<i>Actual</i>)
■	SIRs # Active (<i>Target</i>)
■	Milestone Target

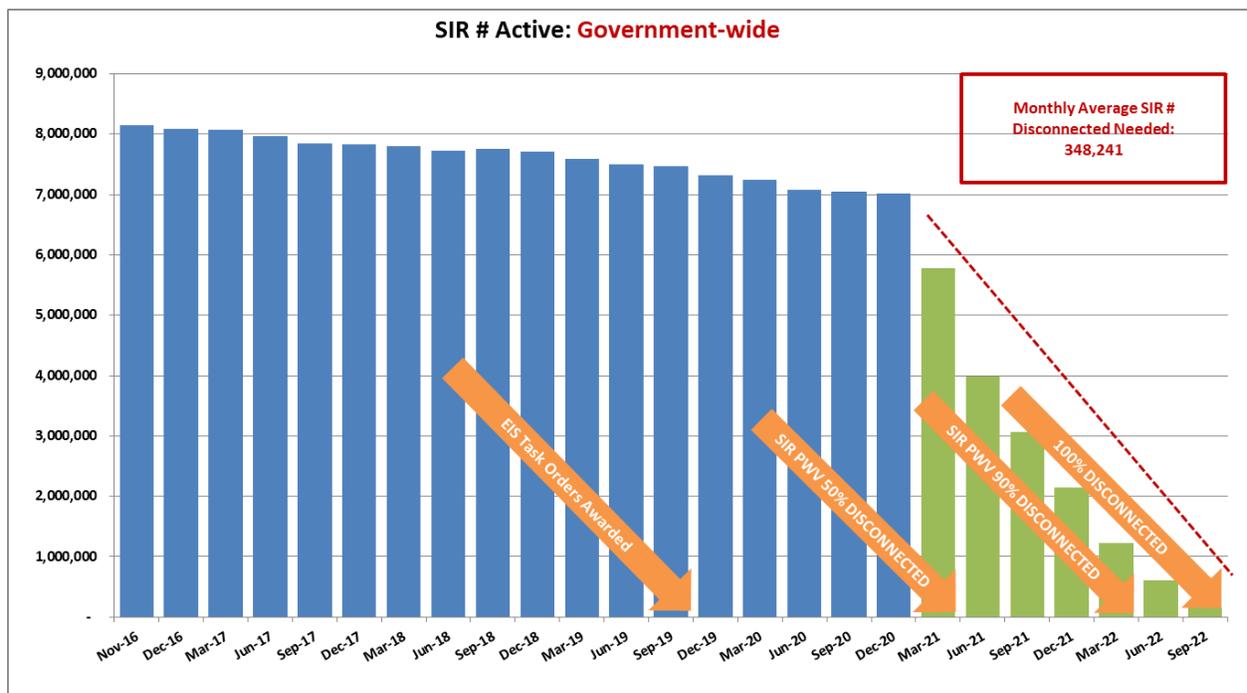


Figure 1. SIR # Active: Government-wide

2.2 Transition Progress Metrics Summary

Table 1 provides a summary of transition progress metrics by agency category. Tribes are broken out separately from small agencies for the purpose of this table. The goal is to reach 100% complete (disconnected) by the date listed.

Table 1. Transition Progress Metrics Summary: Agency Categories

Transition Progress Metrics Summary: Agency Categories							
Tracking Metric	Date Due	Percentage Complete	Total Count	Large Agencies Count	Medium Agencies Count	Small Agencies Count	Native American Tribes Count
Data As Of: 01/31/2021							
Total EIS FO Solicitations Planned			212	105	45	62	
EIS FO Solicitations Passed GSA In-Scope Review	3/31/2019	91.51%	194	102	41	51	
EIS FO Solicitations Issued to Industry	3/31/2019	77.36%	164	85	39	40	
Task Orders Awarded (as defined by Key Metric)	9/30/2019	43.87%	93	58	24	11	
Data As Of: 01/31/2021							
Total Agencies			221	17	25	117	62
Transition 50% Complete (≥50% and <90%)	3/31/2021	17.19%	38	5	6	24	3
Transition 90% Complete (≥90% and <100%)	3/31/2022	4.52%	10	0	2	7	1
Transition 100% Complete (=100%)	9/30/2022	24.89%	55	0	0	23	32

2.3 Agency Transition Scorecards

Agency Scorecards provide an overview of agency transition status, where progress through Task Order (TO) award is measured against the number of Fair Opportunity (FO) solicitations expected; and transition percentage complete is measured against SIRs disconnected based on their PWV for complexity. This section depicts Agency Scorecards for the large and medium agency categories.

This Key identifies the markings used when viewing Agency Transition Scorecards.

Key	
Transition Progress	
	Complete, In Progress/Not Past Due, or Not Started/Not Past Due
	In Progress but Past Due
	Not Started and Past Due

Table 2 reflects transition progress for large agencies.

Note: The key transition milestone of 9/30/2019 for agencies to award EIS TOs has passed. As of the end of this reporting period, large agencies have issued 87 transition-related TO awards based on available data from the Network Hosting Center (NHC). Of these, 58 meet the definition and measurement criteria of “TOs Awarded” as listed in Appendix D.

Table 2. EIS Transition Scorecard: Large Agencies

EIS Transition Scorecard: Large Agencies							
Date:	1/31/2021						
AB Code	Agency	EIS FO Solicitations Passed GSA In-Scope Review	EIS FO Solicitations Issued to Industry	Other than EIS FO Solicitations Issued to Industry (Self-reported)	EIS Task Orders Awarded	Other than EIS Task Orders Awarded	Transition SIR PWV % Completed (Disconnected)
Date Due		03/31/2019			09/30/2019		09/30/2022
1200	DEPARTMENT OF AGRICULTURE	1 of 1	1 of 1	N/A	0 of 1	0 of 0	47.8%
1300	DEPARTMENT OF COMMERCE	2 of 2	2 of 2	N/A	2 of 2	0 of 0	30.5%
9721	DEPARTMENT OF DEFENSE	56 of 59	48 of 59	3 of 3	32 of 59	3 of 3	30.2%
8900	DEPARTMENT OF ENERGY	2 of 2	2 of 2	N/A	0 of 2	0 of 0	39.8%
7500	DEPARTMENT OF HEALTH AND HUMAN SERVICES	2 of 2	2 of 2	N/A	2 of 2	0 of 0	53.2%
7000	DEPARTMENT OF HOMELAND SECURITY	13 of 13	4 of 13	N/A	1 of 13	0 of 0	29.4%
1500	DEPARTMENT OF JUSTICE	2 of 2	2 of 2	N/A	1 of 2	0 of 0	56.5%
1600	DEPARTMENT OF LABOR	2 of 2	2 of 2	N/A	2 of 2	0 of 0	62.3%
1900	DEPARTMENT OF STATE	1 of 1	1 of 1	N/A	1 of 1	0 of 0	32.5%
1400	DEPARTMENT OF THE INTERIOR	3 of 3	3 of 3	N/A	2 of 3	0 of 0	34.5%
2000	DEPARTMENT OF THE TREASURY	6 of 6	6 of 6	N/A	6 of 6	0 of 0	74.7%
6900	DEPARTMENT OF TRANSPORTATION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	36.2%
3600	DEPARTMENT OF VETERANS AFFAIRS	3 of 3	3 of 3	N/A	3 of 3	0 of 0	56.0%
4700	GENERAL SERVICES ADMINISTRATION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	34.7%
1000	JUDICIARY	2 of 2	2 of 2	N/A	0 of 2	0 of 0	36.9%
8000	NATIONAL AERONAUTICS AND SPACE ADMINISTRATION	3 of 3	3 of 3	N/A	2 of 3	0 of 0	19.9%
2804	SOCIAL SECURITY ADMINISTRATION	2 of 2	2 of 2	N/A	2 of 2	0 of 0	45.0%

Table 3 reflects the transition progress for medium agencies.

Note: The key transition milestone of 9/30/2019 for agencies to award EIS TOs has passed. As of the end of this reporting period, medium agencies have issued 31 transition-related TO awards based on available data from the NHC. Of those, 24 meet the definition and measurement criteria of “TOs Awarded” as listed in Appendix D.

Table 3. EIS Transition Scorecard: Medium Agencies

EIS Transition Scorecard: Medium Agencies							
Data As Of:	1/31/2021						
AB Code	Agency	EIS FO Solicitations Passed GSA In-Scope Review	EIS FO Solicitations Issued to Industry	Other than EIS FO Solicitations Issued to Industry (Self-reported)	EIS Task Orders Awarded	Other than EIS Task Orders Awarded	Transition SIR PWV % Completed (Disconnected)
Date Due		03/31/2019			09/30/2019		09/30/2022
9507	COMMODITY FUTURES TRADING COMMISSION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	20.8%
9559	CONSUMER FINANCIAL PROTECTION BUREAU	1 of 1	1 of 1	N/A	1 of 1	0 of 0	65.6%
9100	DEPARTMENT OF EDUCATION	3 of 3	3 of 3	N/A	3 of 3	0 of 0	37.0%
8600	DEPARTMENT OF HOUSING AND URBAN DEVELOPMENT	1 of 1	1 of 1	N/A	0 of 1	0 of 0	37.1%
6800	ENVIRONMENTAL PROTECTION AGENCY	1 of 1	1 of 1	N/A	0 of 1	0 of 0	36.4%
4500	EQUAL EMPLOYMENT OPPORTUNITY COMMISSION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	47.8%
1100	EXECUTIVE OFFICE OF THE PRESIDENT	4 of 4	4 of 4	N/A	3 of 4	0 of 0	99.7%
7800	FARM CREDIT ADMINISTRATION	1 of 2	1 of 2	N/A	0 of 2	0 of 0	52.2%
2700	FEDERAL COMMUNICATIONS COMMISSION	2 of 2	2 of 2	N/A	2 of 2	0 of 0	46.2%
5100	FEDERAL DEPOSIT INSURANCE CORPORATION	0 of 0	0 of 0	N/A	0 of 0	0 of 0	98.3%
2600	FEDERAL RETIREMENT THRIFT INVESTMENT BOARD	1 of 1	1 of 1	N/A	0 of 1	0 of 0	37.4%
0500	GOVERNMENT ACCOUNTABILITY OFFICE	1 of 1	0 of 1	N/A	0 of 1	0 of 0	44.9%
8800	NATIONAL ARCHIVES AND RECORDS ADMINISTRATION	1 of 1	1 of 1	N/A	0 of 1	0 of 0	24.3%
6300	NATIONAL LABOR RELATIONS BOARD	3 of 3	3 of 3	N/A	3 of 3	0 of 0	43.2%
4900	NATIONAL SCIENCE FOUNDATION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	74.3%
3100	NUCLEAR REGULATORY COMMISSION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	89.9%
2400	OFFICE OF PERSONNEL MANAGEMENT	1 of 1	1 of 1	N/A	0 of 1	0 of 0	21.3%
1606	PENSION BENEFIT GUARANTY CORPORATION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	78.2%
6000	RAILROAD RETIREMENT BOARD	5 of 5	4 of 5	N/A	3 of 5	0 of 0	11.1%
5000	SECURITIES AND EXCHANGE COMMISSION	3 of 6	3 of 6	N/A	2 of 6	0 of 0	62.9%
7300	SMALL BUSINESS ADMINISTRATION	1 of 1	1 of 1	N/A	1 of 1	0 of 0	28.6%
6400	TENNESSEE VALLEY AUTHORITY	3 of 3	3 of 3	N/A	0 of 3	0 of 0	46.8%
1800	UNITED STATES POSTAL SERVICE	2 of 2	2 of 2	N/A	1 of 2	0 of 0	20.3%
9568	US AGENCY FOR GLOBAL MEDIA	1 of 1	1 of 1	N/A	0 of 1	0 of 0	40.0%
7200	US AGENCY FOR INTERNATIONAL DEVELOPMENT	1 of 1	1 of 1	N/A	0 of 1	0 of 0	34.7%

2.4 Transition Completion Status

Table 4 shows a list of large and medium agencies that have disconnected 100% of their TI SIRs as reported by Networkx contractors, WITS 3, and the Telecommunications Ordering and Pricing System (TOPS). Both “SIR % Disconnected” and “BV % Reduction” must reach 100% before transition is considered complete.

Note: *To date, no large or medium agencies have disconnected 100% of TI SIRs. A listing of small agencies including Native American Tribes that have disconnected 100% of TI SIRs is provided in Appendix B.*

Table 4. Transition Completion Status: Large and Medium Agencies

Transition Completion Status: Large and Medium Agencies						
Agency Category	AB Code	Agency	SIR % Disconnected	BV % Reduction	Transition Complete	Transition Complete Date
L	NONE					
M	NONE					

3 Fair Opportunity Solicitations

3.1 Fair Opportunity Process for Selecting EIS Contractors

Agencies must follow the FO process to issue solicitations to industry and award TOs. The TCC tracks and reports metrics that drive the process, such as the number of FO solicitations expected [derived from the Agency Transition Plan (ATP), or subsequently in data calls from GSA Solutions Brokers (SBs) the number of FO solicitations that have passed GSA in-scope review, the number of FO solicitations issued to industry, and the award of at least one TO against each FO solicitation.

FO solicitations below the simplified acquisition threshold (SAT) do not require in-scope review but may be reported as part of the total FO solicitations expected by an agency. In these instances, the solicitation is considered to have automatically passed in-scope review once it has been issued to industry.

Table 5 provides a summary of FO solicitation progress.

Table 5. Fair Opportunity Solicitation Progress

Fair Opportunity Solicitation Progress					
Agency Category	EIS - FO Solicitations Expected	EIS - FO Solicitations Passed GSA In-Scope Review	EIS - FO Solicitations Issued to Industry	Other Than EIS - FO Solicitations Expected	Other Than EIS - FO Solicitations Issued to Industry
L	105	102	85	3	3
M	45	41	39	0	0
Total Count	150	143	124	3	3

3.1.1 Fair Opportunity Solicitations Passed GSA In-Scope Review

FO solicitations above the SAT must pass GSA in-scope review prior to being issued to industry. Figure 2 compares the number of FO solicitations expected to those that have passed GSA in-scope review for each of the large agencies. Of the 105 large agency EIS FO solicitations expected, 102 have passed GSA in-scope review (97.1%).

Notes: No large agencies received in-scope determinations this reporting period.

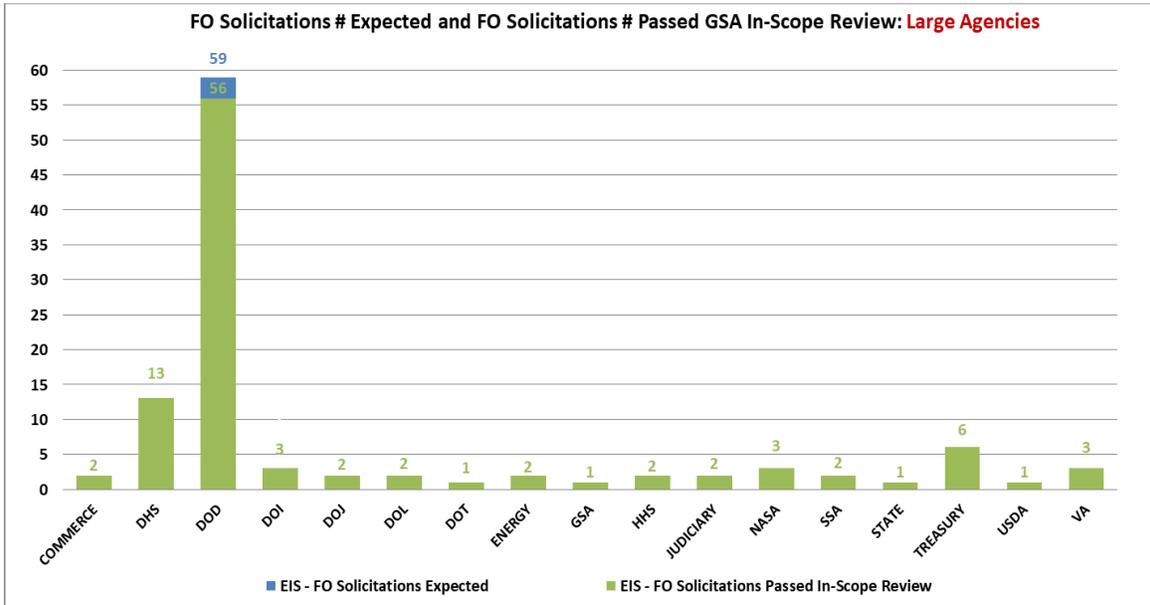


Figure 2. FO Solicitations # Expected and FO Solicitations # Passed GSA In-Scope Review: Large Agencies

Figure 3 compares the number of FO solicitations expected to those that have passed GSA in-scope review for each of the medium agencies. Of the 45 medium agency EIS FO solicitations expected, 41 have passed GSA in-scope review (91.1%).

Note: No medium agencies received in-scope determinations this reporting period.

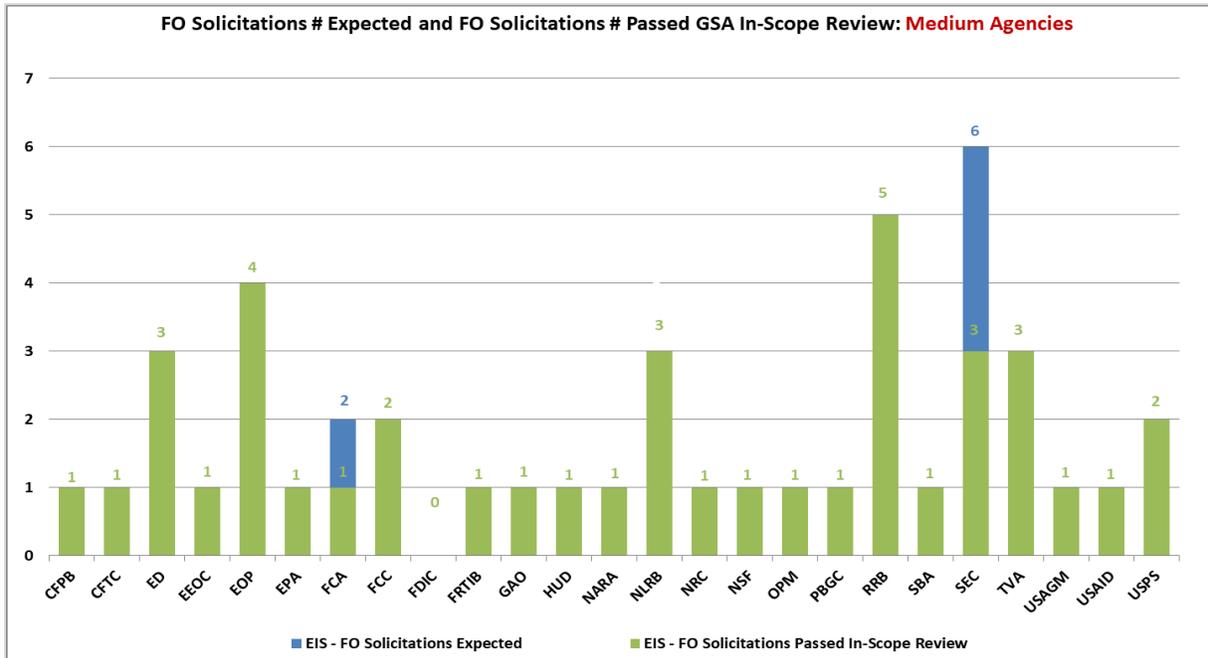


Figure 3. FO Solicitations # Expected and FO Solicitations # Passed GSA In-Scope Review: Medium Agencies

3.1.2 Fair Opportunity Solicitations Issued to Industry

Agencies must issue FO solicitations to industry prior to awarding EIS TOs. The TCC uses data provided by GSA SBs to track and report progress towards this metric. Agency representatives are encouraged to self-report to confirm FO solicitations issued to industry when they elect to use contracts other than EIS. The TCC will reflect this data as “Other than EIS” in Figure 4 below.

Figure 4 illustrates the number of FO solicitations expected and issued to industry for large agencies. Of the 105 large agency EIS FO solicitations expected, 85 have been issued to industry (81.0%). DOD has issued 3 of 3 FO solicitations on vehicles other than EIS.

Note: No large agencies issued solicitations to industry this reporting period.

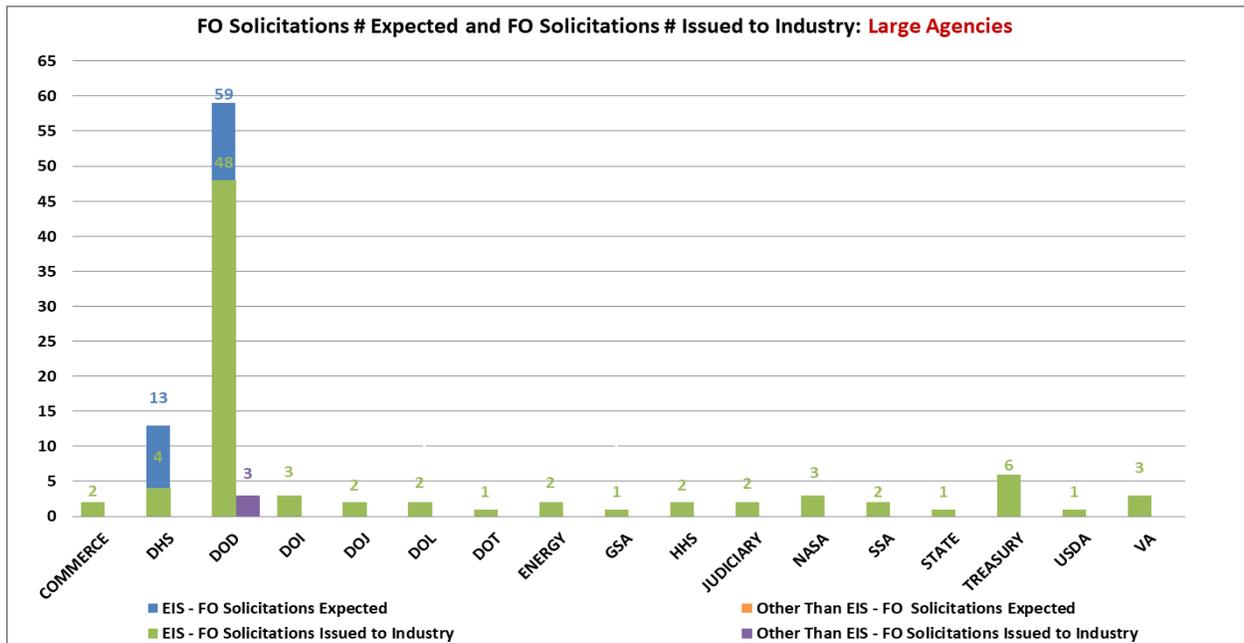


Figure 4. FO Solicitations # Expected and FO Solicitations # Issued to Industry: Large Agencies

Figure 5 illustrates the number of FO solicitations expected and issued to industry for medium agencies. Of the 45 medium agency EIS FO solicitations expected, 39 have been issued to industry (86.7%). Medium agencies have not self-reported the release of FO solicitations on contract vehicles other than EIS.

Note: *Tennessee Valley Authority (TVA) issued three (3) solicitations to industry and US Agency for Global Media (USAGM) issued one solicitation to industry this reporting period.*

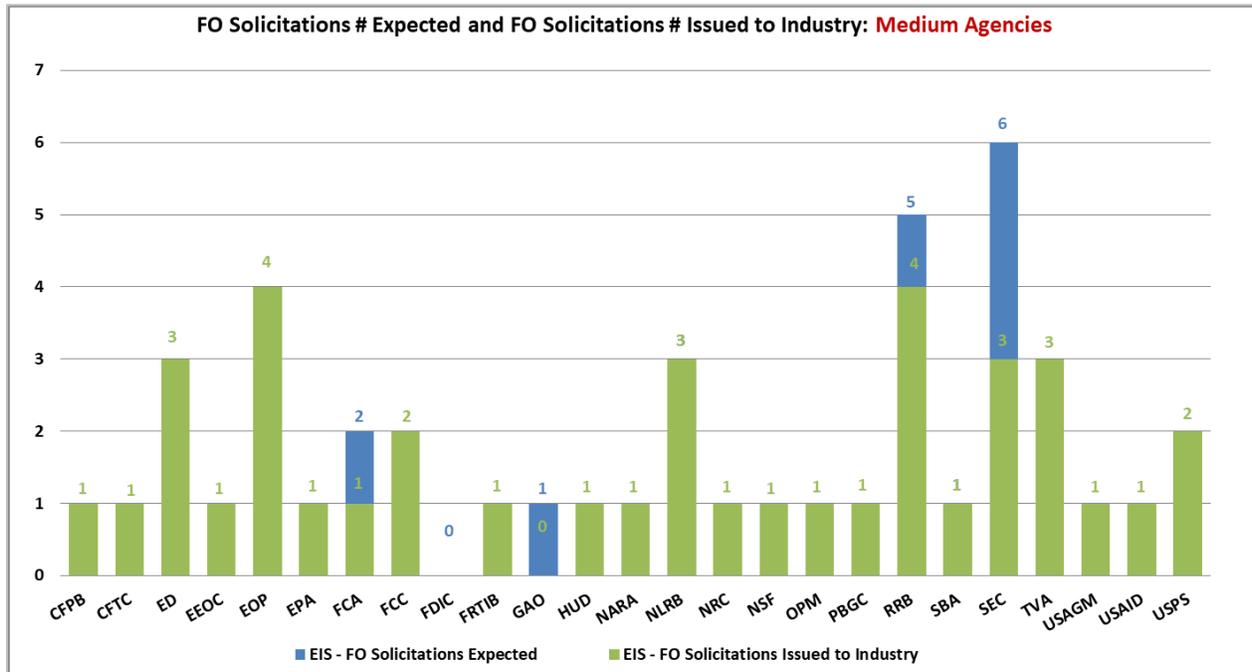


Figure 5. FO Solicitations # Expected and FO Solicitations # Issued to Industry: Medium Agencies

3.1.3 EIS Task Orders Awarded

An agency indicates selection of an EIS contractor by awarding at least one TO for each solicitation. Since an FO decision could result in multiple TOs, it is not possible to ascertain that all TOs have been awarded for any given FO solicitation. When an agency has awarded at least one TO for an FO solicitation, the EIS contractor(s) will report the TO award(s) to GSA, and GSA will register this step as complete for that FO solicitation.

Table 6 provides the number of EIS TOs awarded by large agencies during this reporting period.

Note: Seven (7) new large agency TO awards were reported in the NHC this period. TO awards that meet the definition and measurement criteria listed in Appendix D are highlighted in green.

Table 6. EIS Task Order Award Status: Large Agencies

AB Code	Agency	TO Award Date	TO #	EIS Contractor	Latest TO Revision #	Latest TO Revision Date
9721	DEPARTMENT OF DEFENSE*	01/05/2021	HC101321F0024	Granite	1	01/14/2021
9721	DEPARTMENT OF DEFENSE	01/06/2021	HC101321FA183	Granite	1	01/12/2021
9721	DEPARTMENT OF DEFENSE	01/05/2021	HC101321FA991	Granite	1	01/11/2021
9721	DEPARTMENT OF DEFENSE	01/05/2021	HC101321FB069	Granite	1	01/11/2021
9721	DEPARTMENT OF DEFENSE	01/06/2021	HC101321FB074	CenturyLink	1	01/29/2021
9721	DEPARTMENT OF DEFENSE	01/19/2021	HC101321FB276	Granite	1	01/27/2021
9721	DEPARTMENT OF DEFENSE	01/19/2021	HC101321FB532	Granite	1	01/26/2021

*indicates the first TO award issued against an FO solicitation

Table 7 provides the number of TOs awarded by medium agencies this reporting period.

Note: One new medium agency TO awards was reported in the NHC this period. TO awards that meet the definition and measurement criteria listed in Appendix D are highlighted in green.

Table 7. EIS Task Order Award Status: Medium Agencies

AB Code	Agency	TO Award Date	TO #	EIS Contractor	Latest TO Revision #	Latest TO Revision Date
2700	FEDERAL COMMUNICATIONS COMMISSION*	12/29/2020	273FCC21F0011	AT&T	1	01/04/2021

*indicates the first TO award issued against an FO solicitation

4 Transition Execution Progress

Once TOs have been awarded, agencies work directly with EIS contractors to execute the transition of services. Transition is considered complete when all SIRs from expiring contracts have been disconnected and BV has been reduced to zero.

4.1 Government-wide

This section identifies transition progress Government-wide for the following metrics: SIR disconnected, SIR PWV disconnected, and BV reduction. Figure 6 illustrates Government-wide trending of these metrics where the goal for all measures is 100%.

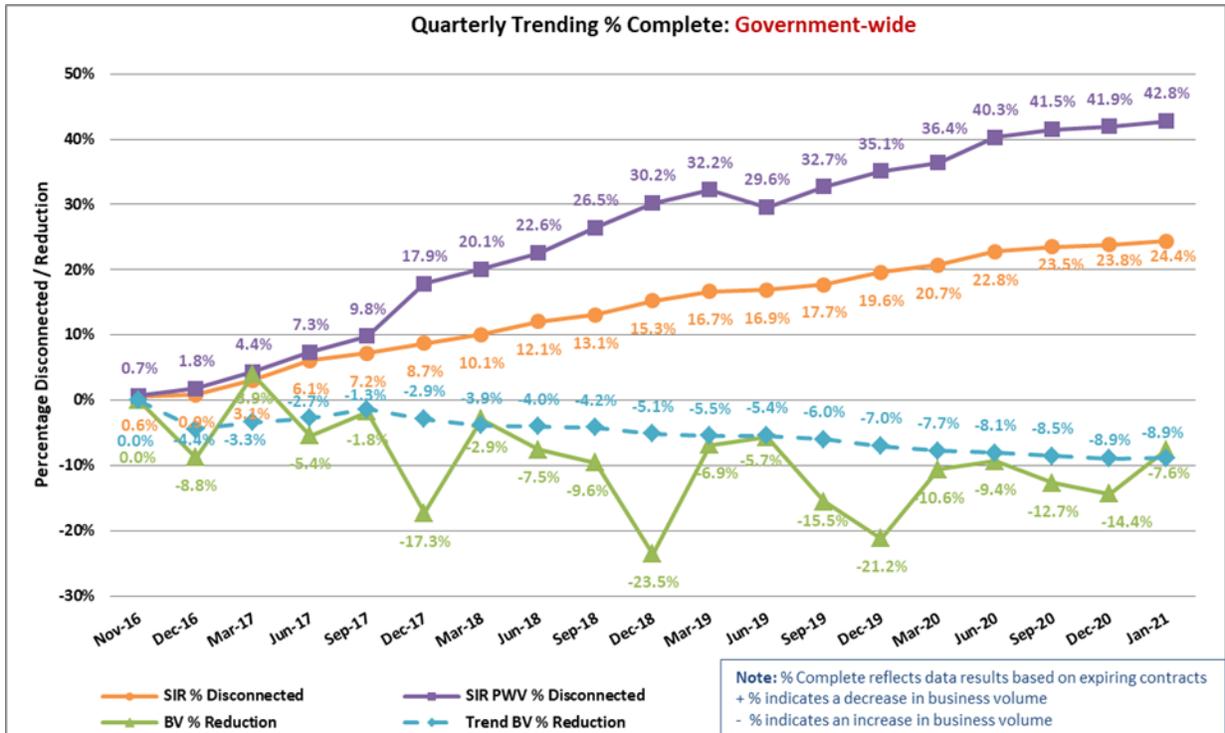


Figure 6. Quarterly Trending % Complete: Government-wide

4.2 Transition Progress – Agency Category

This section identifies transition progress by agency category based on SIR disconnected and SIR PWV disconnected metrics.

4.2.1 Transition Progress - Large Agencies

Figure 7 illustrates the comparison between the baseline SIR counts and current SIR counts for each of the large agencies.

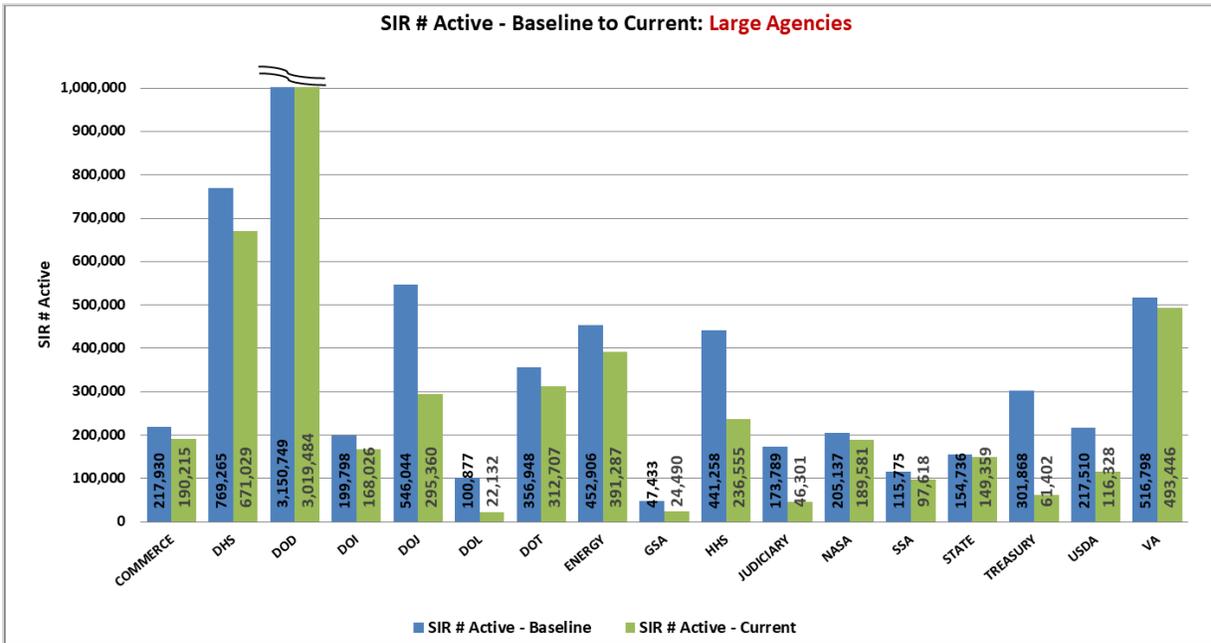


Figure 7. SIR # Active – Baseline to Current: Large Agencies

Figure 8 illustrates the comparison between the baseline SIR PWV counts and current SIR PWV counts for each of the large agencies.

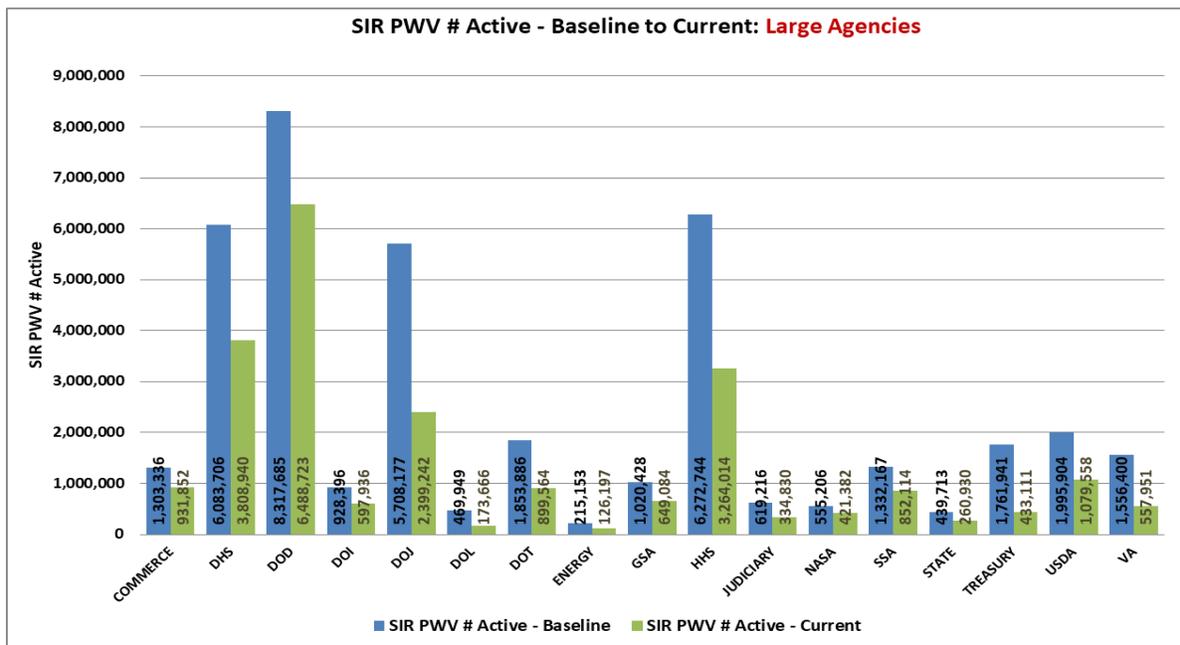


Figure 8. SIR PWV # Active – Baseline to Current: Large Agencies

4.2.2 Transition Progress - Medium Agencies

Figure 9 illustrates the comparison between the baseline SIR counts and current SIR counts for each of the medium agencies.

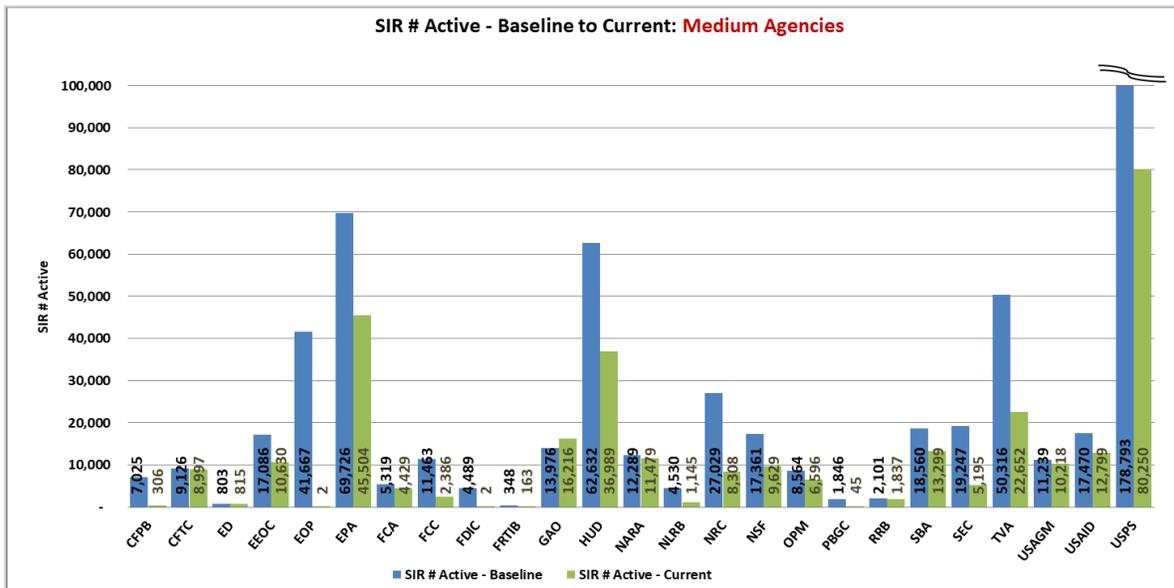


Figure 9. SIR # Active – Baseline to Current: Medium Agencies

Figure 10 illustrates the comparison between the baseline SIR PWV counts and current SIR PWV counts for each of the medium agencies.

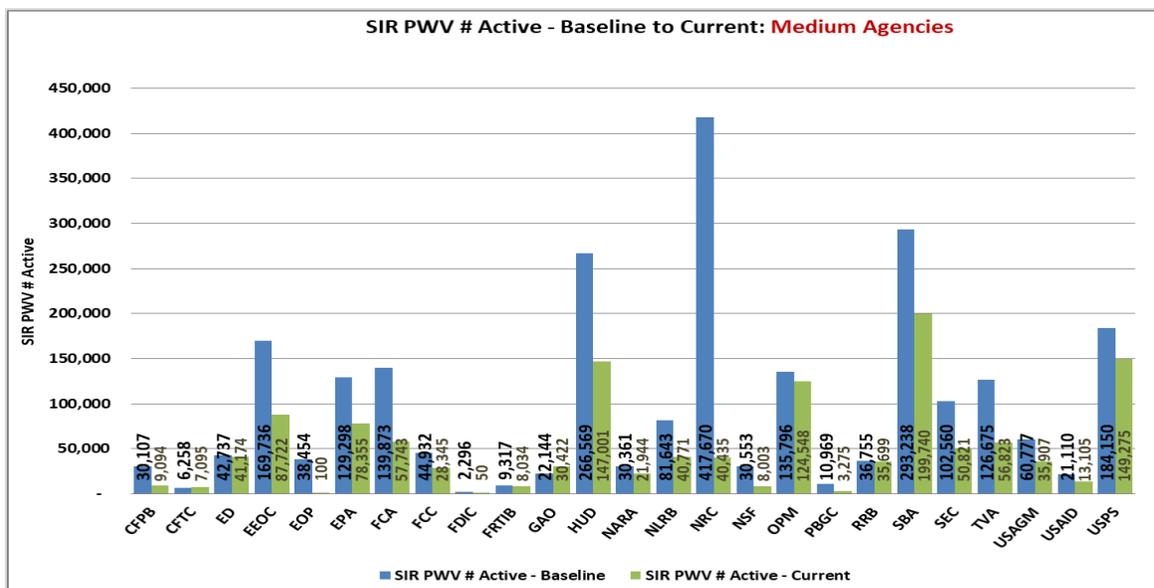


Figure 10. SIR PWV # Active – Baseline to Current: Medium Agencies

4.3 Transition Closeout

As a condition of extending the expiring Networkx, WITS 3, and GSA RLS contracts, GSA requires that agencies meet certain critical milestones to be eligible to use the extensions. GSA is executing a Transition Closeout project to limit the agencies that are using the

extended contracts and to disconnect those that are no longer authorized and removed from the Networks Authorized User List (NAUL). GSA is conducting the disconnects in phases and determines the phasing based on the agency's completion of awarded TOs on EIS, other indications of activity, and progress in transition, along with considering other special circumstances.

Figure 11 reflects status of the Transition Closeout project by phase. Transition complete is defined as SIRs 100% disconnected and BV = \$0.

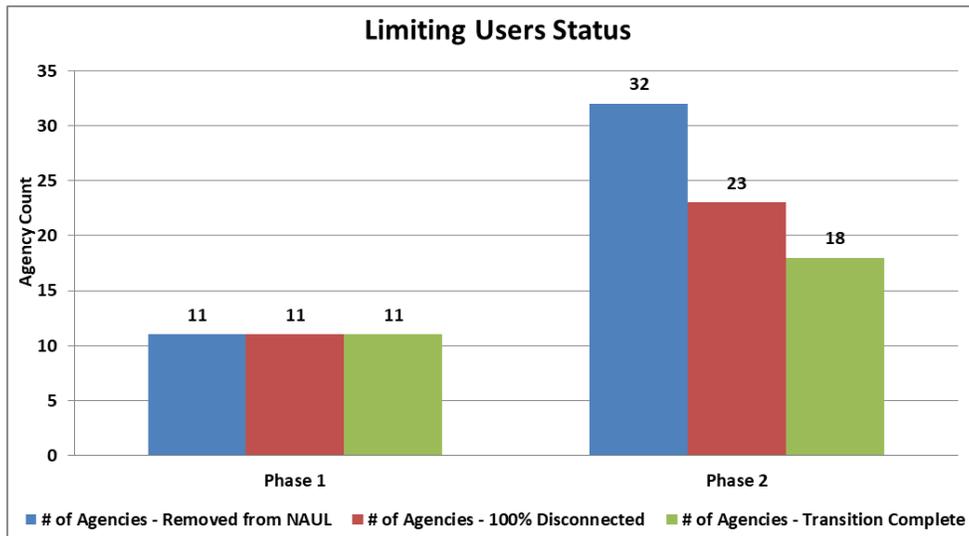


Figure 11. Limiting Users Status

Figure 12 tracks the cumulative status of the Transition Closeout project by month.

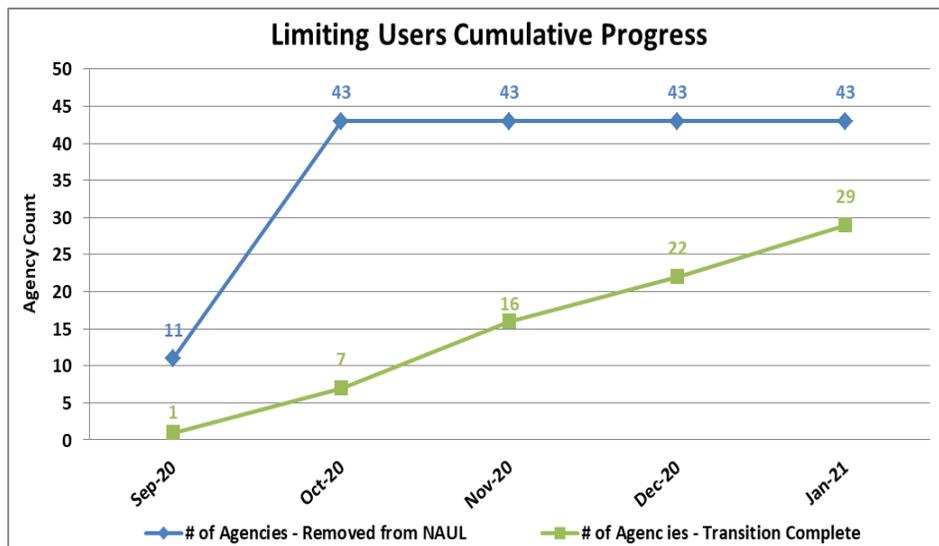


Figure 12. Limiting Users Cumulative Progress

Appendix A – Acronyms

Acronym	Definition
AB	Agency Bureau
ATP	Agency Transition Plan
ATS	Agency Transition Sponsor
BAC	Billing Account Code
BV	Business Volume
CFPB	Consumer Financial Protection Bureau
CFTC	Commodity Futures Trading Commission
CIO	Chief Information Officer
CLIN	Contract Line Item Number
DC	District of Columbia
DHS	Department of Homeland Security
DOD	Department of Defense
DOI	Department of the Interior
DOJ	Department of Justice
DOL	Department of Labor
DOT	Department of Transportation
ED	Department of Education
EEOC	Equal Employment Opportunity Commission
EIS	Enterprise Infrastructure Solutions
E-MORRIS	Enhanced Monthly On-Line Records and Reports of Information Technology Services
EOP	Executive Office of the President
EPA	Environmental Protection Agency
FBI	Federal Bureau of Investigation
FCA	Farm Credit Administration
FCC	Federal Communications Commission
FO	Fair Opportunity
FDIC	Federal Deposit Insurance Corporation
FRTIB	Federal Retirement Thrift Investment Board
FY	Fiscal Year
GAO	Government Accountability Office
GSA	General Services Administration
HHS	Department of Health and Human Services
HUD	Department of Housing and Urban Development
IAA	Interagency Agreement
IAG	Infrastructure Advisory Group
ITT	Integrated Transition Team
LMS	Large, Medium, Small
LTM	Lead Transition Manager
LSA	Local Service Agreement
NARA	National Archives and Records Administration
NASA	National Aeronautics and Space Administration
NAUL	Network Authorized User List
NBIP-VPNS	Network-Based Internet Protocol Virtual Private Network Service
NHC	Network Hosting Center
NLRB	National Labor Relations Board
NRC	Nuclear Regulatory Commission
NSF	National Science Foundation
OPM	Office of Personnel Management
PBGC	Pension Benefit Guaranty Corporation
POC	Point of Contact
PWV	Proportional Weighted Value
RLS	Regional Local Service
RRB	Railroad Retirement Board

Acronym	Definition
SAT	Simplified Acquisition Threshold
SB	Solutions Broker
SBA	Small Business Administration
SEC	Securities Exchange Commission
SIR	Service Instance Record
SSA	Social Security Administration
TCC	Transition Coordination Center
TI	Transition Inventory
TO	Task Order
TOCO	Transition Ordering Contracting Officer
TOPS	Telecommunications Ordering and Pricing System
TPTR	Transition Progress Tracking Report
TSID	Telephone System Identification
TVA	Tennessee Valley Authority
USAGM	US Agency for Global Media
USAID	US Agency for International Development
USDA	US Department of Agriculture
USPS	United States Postal Service
VA	Department of Veterans Affairs
WITS	Washington Interagency Telecommunications System

Appendix B – Transition Completion Status: Small Agencies including Native American Tribes


Transition Completion Status: Small Agencies including Native American Tribes						
Agency Category	AB Code	Agency	SIR % Disconnected	BV % Reduction	Transition Complete	Transition Complete Date
Small Agencies						
S	6908	AMTRAK	100.0%	100.0%	YES	Jan 2021
S	4602	APPALACHIAN REGIONAL COMMISSION	100.0%	100.0%	YES	Jan 2021
S	1294	MILK MARKETING ASSOCIATION	100.0%	100.0%	YES	Jan 2021
S	0065	STATUE OF LIBERTY ELLIS ISLAND FOUNDATION	100.0%	100.0%	YES	Jan 2021
S	9549	MORRIS K UDALL AND STEWART L UDALL FOUNDATION	100.0%	100.0%	YES	Dec 2020
S	9542	OFFICE OF GOVERNMENT ETHICS	100.0%	100.0%	YES	Dec 2020
S	0084	NATIONAL BUILDING MUSEUM	100.0%	100.0%	YES	Sep 2020
S	4952	NATIONAL CENTER FOR ATMOSPHERIC RESEARCH	100.0%	100.0%	YES	Sep 2020
S	3312	JOHN F KENNEDY CENTER FOR THE PERFORMING ARTS	100.0%	100.0%	YES	Aug 2020
S	0814	CONGRESSIONAL BUDGET OFFICE	100.0%	100.0%	YES	Dec 2019
S	1917	INTERNATIONAL BOUNDARY COMMISSION US AND CANADA	100.0%	100.0%	YES	Sep 2019
S	4953	US ARCTIC RESEARCH COMMISSION	100.0%	100.0%	YES	Aug 2019
S	0064	PAN AMERICAN HEALTH ORGANIZATION	100.0%	100.0%	YES	Apr 2019
S	4883	DWIGHT D EISENHOWER MEMORIAL COMMISSION	100.0%	100.0%	YES	Mar 2019
S	9533	BARRY GOLDWATER SCHOLARSHIP AND EXCELLENCE IN EDUCATION FOUNDATION	100.0%	100.0%	YES	Feb 2019
S	5600	CENTRAL INTELLIGENCE AGENCY	100.0%	100.0%	YES	Nov 2017
S	9574	COMMISSION ON THE NATIONAL MOMENT OF REMEMBRANCE	100.0%	100.0%	YES	Oct 2017
S	7618	CHRISTOPHER COLUMBUS FELLOWSHIP FOUNDATION	100.0%	100.0%	YES	Sep 2017
S	4895	COMMISSION FOR INTERNATIONAL RELIGIOUS FREEDOM	100.0%	100.0%	YES	Jul 2017
S	9551	DIRECTOR OF NATIONAL INTELLIGENCE	100.0%	100.0%	YES	Nov 2016
S	9565	FEDERAL COORDINATOR ALASKA NATURAL GAS TRANSPORTATION PROJECTS	100.0%	100.0%	YES	Nov 2016
S	1252	GRADUATE SCHOOL USA	100.0%	100.0%	YES	Nov 2016
S	9561	RECOVERY ACCOUNTABILITY AND TRANSPARENCY BOARD	100.0%	100.0%	YES	Nov 2016
Native American Tribes						
T	NATA	TANANA CHIEF TRIBE (NATA)	100.00%	98.2%	NO	
T	NA32	COLUSA INDIAN COMMUNITY (NA32)	100.00%	96.4%	NO	
T	NC10	PONCA TRIBE OF NEBRASKA (NC10)	100.00%	79.5%	NO	
T	1158	MORONGO BAND OF CAHUILLA INDIANS (1158)	100.00%	77.0%	NO	
T	NA41	CENTRAL COUNCIL TLINGIT AND HAIDA INDIAN TRIBES OF ALASKA (NA41)	100.0%	100.0%	YES	Jan 2021
T	NA05	CHIEF LESCHI SCHOOLS (NA05)	100.0%	100.0%	YES	Jan 2021
T	NC02	NAVAJO TRIBAL UTILITIES AUTHORITY (NC02)	100.0%	100.0%	YES	Jan 2021
T	NB18	HOOPA VALLEY TRIBE OF CALIFORNIA (NB18)	100.0%	100.0%	YES	Dec 2020
T	NB16	RED LAKE BAND OF CHIPPEWA INDIANS (NB16)	100.0%	100.0%	YES	Dec 2020
T	NA29	SQUAXIN ISLAND TRIBE (NA29)	100.0%	100.0%	YES	Dec 2020
T	NC21	UTE MOUNTAIN TRIBE (NC21)	100.0%	100.0%	YES	Dec 2020
T	NA47	GUIDIVILLE RANCHERIO (NA47)	100.0%	100.0%	YES	Nov 2020
T	NA61	HAVASUPAI TRIBE (NA61)	100.0%	100.0%	YES	Nov 2020
T	NAK0	KARUK TRIBE OF CALIFORNIA (NAK0)	100.0%	100.0%	YES	Nov 2020

Transition Completion Status: Small Agencies including Native American Tribes

Agency Category	AB Code	Agency	SIR % Disconnected	BV % Reduction	Transition Complete	Transition Complete Date
T	NA37	KICKAPOO TRIBE (NA37)	100.0%	100.0%	YES	Nov 2020
T	NA42	NARRAGANSETT TRIBE OF RHODE ISLAND (NA42)	100.0%	100.0%	YES	Nov 2020
T	NC08	ROSEBUD SIOUX TRIBE (NC08)	100.0%	100.0%	YES	Nov 2020
T	NA49	SHAWNEE TRIBE (NA49)	100.0%	100.0%	YES	Nov 2020
T	NA44	WHITE EAGLE HEALTH CENTER (NA44)	100.0%	100.0%	YES	Nov 2020
T	NA69	WHITE MOUNTAIN APACHE TELECOM (NA69)	100.0%	100.0%	YES	Nov 2020
T	GRLA	GREAT LAKES INTER-TRIBAL COUNCIL (GRLA)	100.0%	100.0%	YES	Oct 2020
T	NA14	PENOBSCOT INDIAN NATION (NA14)	100.0%	100.0%	YES	Oct 2020
T	NA33	MECHOOPDA INDIAN TRIBE (NA33)	100.0%	100.0%	YES	Aug 2020
T	NA57	YUOK TRIBE (NA57)	100.0%	100.0%	YES	Aug 2020
T	NA03	CONFEDERATED TRIBES OF THE GRANDE RONDE COMMUNITY OF OREGON (NA03)	100.0%	100.0%	YES	Feb 2020
T	NAS0	STILLAGUAMISH TRIBE (NAS0)	100.0%	100.0%	YES	Feb 2020
T	GLIF	GREAT LAKES INDIAN FISH AND WILDLIFE (GLIF)	100.0%	100.0%	YES	Dec 2019
T	NAS1	STILLAGUAMISH TRIBE (NAS1)	100.0%	100.0%	YES	Jun 2019
T	NAS2	STILLAGUAMISH TRIBE (NAS2)	100.0%	100.0%	YES	May 2019
T	NC06	MOHICAN NORTH STAR OPERATIONS (NC06)	100.0%	100.0%	YES	May 2018
T	NC12	MUCKLESHOOT INDIAN (NC12)	100.0%	100.0%	YES	May 2018
T	NA56	UNITED SOUTH AND EASTERN TRIBES (NA56)	100.0%	100.0%	YES	Jun 2017

Appendix C – Transition Progress Milestones Gantt Chart

The below Gantt Chart illustrates key milestones and target dates established for tracking the progress of transition.

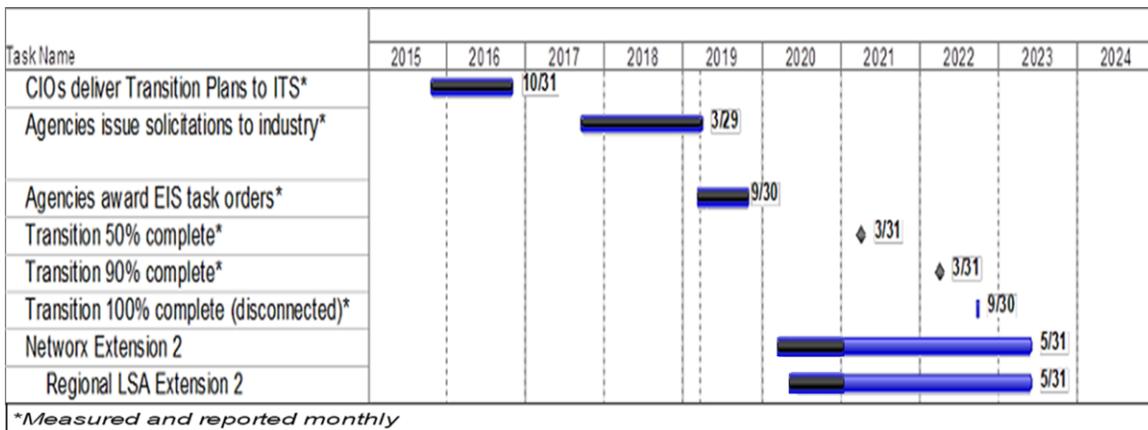

Appendix D – Key Metrics

Tracking Metric	Target Date	Definition	Measurement
ITT Assigned	6/30/2016	Agency Transition Sponsor (ATS), Transition Ordering Contracting Officer (TOCO), and Lead Transition Manager (LTM) assigned by agency as part of the Integrated Transition Team (ITT)	TCC received Transition Team POC info from Agency CIO or other known contact
TI Access	10/31/2016	Agency access to Transition Inventory (TI) data	Agency has at least one E-MORRIS user account to view/confirm TI data
IAA Signed	5/31/2017	Interagency Agreement (IAA) signed	TCC received IAA signed by Agency and GSA; or IAA not required
ATP Submitted	10/31/2016	Agency Transition Plan (ATP) submitted	TCC received ATP signed by ATS and it includes at least the info from the outline in the Transition Handbook
Solicitations Issued to Industry	3/31/2019	Agencies will issue EIS solicitations, that have passed scope review, to industry for proposals	Agency reports to GSA as solicitations are issued to industry for proposals. Solutions Brokers will collect data and make available to the TCC through the solicitation forecast by the end of each month <u>Note:</u> After this target date, GSA reserves the option to cut off GSA-funded Transition Ordering Assistance (TOA) support for agencies' solicitation development. GSA will work with agencies unable to meet this date on an individual basis. GSA will process contract modifications on Networx and WITS 3 (direct order contracts) only for mission essential services.
Task Orders Awarded	9/30/2019	At least one task order awarded for each solicitation as reported by EIS contractor through the Network Hosting Center (NHC)	As EIS contractors receive task orders, they report them to GSA, and the TOs are recorded in the NHC; GSA will track that at least one TO is awarded for each solicitation the agency has forecasted <u>Note:</u> After this target date, GSA will cease adding services on Regional Local Service contracts (aka LSAs) that comprise the full service program
Transition 50% Complete	3/31/2021	Proportional Weighted Value (PWV) percentage disconnected	50% of TI is disconnected as reported by Networx contractors, WITS 3 PMO, and TOPS based on SIR PWV disconnects
Transition 90% Complete	3/31/2022	PWV percentage disconnected	90% of TI is disconnected as reported by Networx contractors, WITS 3 PMO, and TOPS based on SIR PWV disconnects
Transition 100% Complete (disconnected)	9/30/2022	100% of services disconnected	100% of TI is disconnected as reported by Networx contractors, WITS 3 PMO, and TOPS based on SIR PWV disconnects

Appendix E – Key Definitions

Key Term	Key Definition
All Agency Inventory (AAI)	A detailed inventory that extends current TI data to include individual CLINs, features, equipment, bandwidth, and other data not currently included in TI; Data is primarily based on contractor inventory, billing, and orders for Networx, WITS 3, and RLS contracts
Business Volume (BV)	The amount billed by the contractors for services, including adjustments, taxes and fees; sometimes includes adjustments made by GSA
BV Reduction	A transition execution metric that compares current BV to the initial BV
Confirmation of Validated Inventory	<p>Confirmation means a transition entity has determined that its TI records accurately represent the service instances that need to be transitioned from the expiring Networx, WITS 3, and GSA RLS contracts. The confirmation process is exception-based, and the transition entity should only report exceptions where applicable.</p> <p>Each transition entity is expected to retrieve, review and confirm its validated transition inventory). The TI User Guide is available on the EIS website; this Guide can assist transition entity users with accessing E-MORRIS and viewing their inventory data. Transition entities do not need to re-validate the inventory; they just need to confirm the inventory. The method of communication is for the transition entity to place a statement in its ATP by October 2016 stating it has reviewed and confirmed the validated inventory.</p>
Fair Opportunity (FO) Solicitations Expected	Count based on information agencies provided in their ATP (or subsequently in a data call from Solutions Brokers.
FO Solicitations Issued to Industry	Count of solicitations that have been released to EIS contractors
FO Solicitations Passed In-Scope Review	Count defined as passing a GSA in-scope review
Large, Medium, Small (LMS) Agency Categories	In the context of the transition program, agencies with inventory that must be transitioned are categorized into three main categories: Large agencies, Medium agencies, and Small agencies. The Large agencies represent a group of 17 agencies each billing an average annual BV of more than \$10 million in FY12 through FY15 on the Networx contracts. The Medium agencies represent a group of 25 agencies each with an average annual of less than \$10 million, but over \$1 million. Finally, the Small agencies represent a group of agencies each with an average annual of less than \$1 million.
Page View	The number of times a visitor views a webpage on the GSA website (Note: Each webpage a visitor views is tracked as one page view; and if a visitor navigates to a different page and returns to the original page, or refreshes the page, a second page view will be recorded.)
Proportional Weighted Value (PWV)	Values assigned to SIRs based on the relative difficulty of transitioning that particular service (simple services, such as calling cards, reflect a low PWV; while more complex services such as NBIP-VPNS hold a higher value)
Service Instance Record (SIR)	Level of inventory tracking record that provides GSA and transition entities with a consistent measure to track services as they transition from expiring contracts; Represents a summarized roll-up of a base service and the associated supporting/feature CLINs, supports transition entity transition planning, and provides a mechanism for the transition entities and GSA to track the progress of transition from Networx, WITS 3, and GSA RLS contracts
SIR Disconnected	A transition execution metric that measures reductions in SIR counts until there are no active SIRs remaining (100% disconnected)
TPTR Report Grouping Levels	<ul style="list-style-type: none"> • Government-wide: This grouping represents the aggregate of all government agencies collectively. • Program: The program category view reflects the three main contract groups that are expiring and must transition. These groups are: <ul style="list-style-type: none"> • Networx (Universal and Enterprise) • GSA RLS • WITS 3 • Agency Category: This grouping represents the levels at which agencies are grouped for reporting purposes within this report. There are three categories: Large agencies,

Key Term	Key Definition
	<p>Medium agencies, and Small agencies (See LMS key term and definition above).</p> <ul style="list-style-type: none"> • Contractor: The contractor category view reflects a grouping by individual contractor. All GSA RLS contractors are grouped together as “Other.” The contractor groups are: <ul style="list-style-type: none"> • AT&T • CenturyLink • Level 3 • GSA RLS • Sprint • Verizon • Service Category: This represents all services under the expiring Networx, WITS 3, and RLS contracts; and are grouped into the following ten categories of services: <ul style="list-style-type: none"> • Access • Communications Transport Services • IP Based Services • Management and Application Services • Miscellaneous • Optical Services • Security Services • Special Services • Taxes • Wireless Services
Transition	The movement from the expiring Networx, WITS 3 and GSA RLS vehicles to the replacement EIS contracts
Transition Complete	Transition Complete represents each transition entity’s achievement of transition including 100% of SIRs disconnected and 100% of BV reduction.
Transition Entity	<p>The level at which the agencies intend to manage their organization’s transition activities is referred to as a “transition entity.”</p> <p>Some agencies may manage their transition activities at the agency level, while others may manage transition at the sub agency level. Still others may separate only one or two sub agencies from the overall parent and manage their transitions accordingly.</p> <p>The Transition Entities List is located on the GSA EIS Transition webpage.</p>
Transition Inventory (TI)	A collection of inventory records at the service instance level, reflecting active services that must be transitioned off the expiring Networx, WITS 3 and GSA RLS contracts; TI will be updated, at least monthly, to reflect services as they are added, changed, or disconnected from the expiring contracts. This data is available to agency customers through the E-MORRIS online application.
Validation	Describes the activities associated with normalizing, comparing and reconciling the data at the service instance level. Validated data is for transition planning and tracking purposes and is not intended for placing transition orders.
